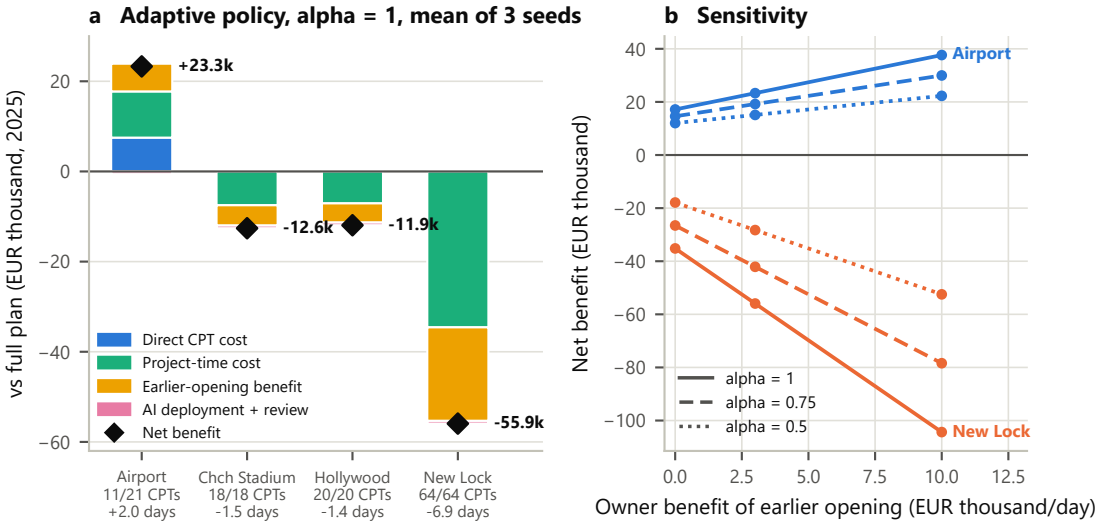
a Adaptive policy, alpha = 1, mean of 3 seeds
vs full plan (EUR thousand, 2025)
20
0
−20
−40
−60
+23.3k
-12.6k
-11.9k
-55.9k
Direct CPT cost
Project-time cost
Earlier-opening benefit
AI deployment + review
Net benefit
Airport
11/21 CPTs
+2.0 days
Chch Stadium
18/18 CPTs
-1.5 days
Hollywood
20/20 CPTs
-1.4 days
New Lock
64/64 CPTs
-6.9 days
b Sensitivity
Net benefit (EUR thousand)
40
20
0
−20
−40
−60
−80
−100
Airport
New Lock
alpha = 1
alpha = 0.75
alpha = 0.5
0.0
2.5
5.0
7.5
10.0
12.5
Owner benefit of earlier opening (EUR thousand/day)
